

Cap-Brulé's new wastewater treatment facility PROJECT UPDATE No. 8 September 2023

"The Dunes" approach concept
by Acre Architects Inc.




Environmental risk assessment & overall project coordination

- As part of the Certificate of Determination of the EIA process, in September 2023, Englobe provided an updated report to the N.B. Department of Environmental and Local Government.
- The funding for Contract 1 and Contract 2 was secured. Due to the high price from the previous Contract 1 tender process, the procurement of major equipment was moved to Contract 2. Therefore, a new strategy is in place, where Contract 2 is divided in two phases: 2A — *Pre-selection and pre-purchasing of major equipment*, and 2B — *Construction of lagoons and outfall*.

Contract 1 – Construction of the new headworks building

- Detailed design is under revision, based on project strategy. **Expectation is for tender to be advertised for the end of November 2023.**
- **Construction scheduled for beginning of spring 2024.**

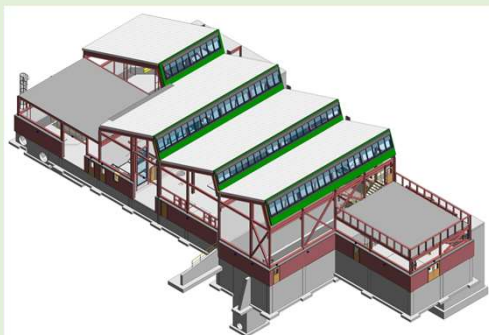

New headworks building looking from southeast

Contract 2 – Construction of lagoons, outfall and major equipment

- Contract 2 design is 100% complete.
- As part of phase 2A — *Pre-selection and pre-purchasing of major equipment*, the **expectation is for the tender to be advertised by the end of October 2023.**
- For Phase 2B — *Construction of lagoons and outfall*, **tendering is tentatively scheduled for February 2025.**

Next steps:

Contract 1:

- Design review
- Tender advertisement scheduled for November 2023

Contract 2:

- Pre-selection of major equipment – Tender advertisement scheduled for October 2023
