


Cap-Brulé's New Wastewater Treatment Facility

PROJECT UPDATE No. 26, September 2025



Construction of the Headworks Building:

- Ongoing activities include backfilling, formwork, rebar, concrete pouring, installation of steel ladders and landings, waterproofing and insulation of structures, and installation of pipes.
- Concrete work progressed with formwork, rebar installation, concrete pours, backfilling, waterproofing and insulation on the UV/Mechanical room.
- Concrete work progressed with formwork, rebar installation, concrete pours on the UV Slab and Lift Station. Concluding the installation of bollards around the propane base.
- Concluding the structural steel installation (ladders and landings) in Influent and Effluent wet wells.
- Installation of the forcemain (pressurized sewer pipe) and excavation for the buried airline pipes.

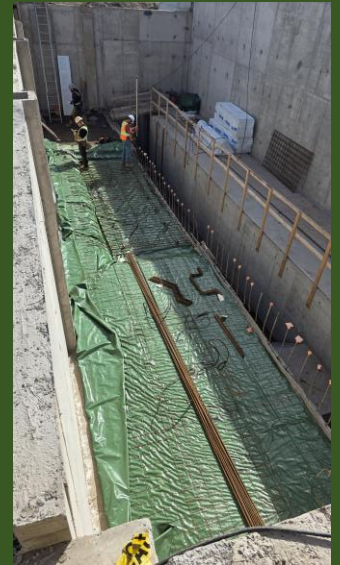

ENGLOBE
