


Cap-Brulé's New Wastewater Treatment Facility

PROJECT UPDATE No. 37, August 2026

Construction of the Headworks Building:

- Completed various building and equipment support elements, including vent supports, housekeeping pads, overhead door preparations, exterior lighting modifications, and structural steel touch-up painting.
- Substantially completed headcell construction activities, with remaining work focused on installation of suction and water lines prior to concrete placement.
- Advanced roofing and building enclosure works, including completion of major air barrier installations, dens deck placement, louvre installations.
- Continued mechanical, process, and electrical installations throughout the facility, including process piping, blower intake installation, duct modifications, electrical rough-ins, lighting systems, and fire alarm infrastructure.

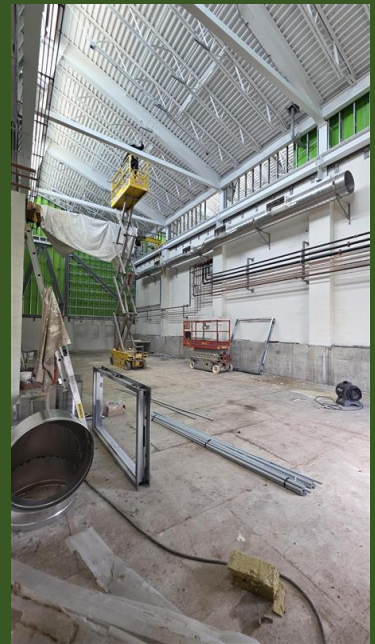

ENGLOBE
