Cap-Brulé's New Wastewater Treatment Facility
PROJECT UPDATE No. 38, September 2026

GREATER SHEDIAC SEWERAGE COMMISSION
DES ÉGOUTS SHEDIAC ET BANLIEUES




"The Dunes" approach concept by Acre Architects Inc.

Construction of the Headworks Building:

- Substantially completed roofing, louvre installations, and building enclosure works, resulting in a weather-tight structure with final door installations.
- Ongoing mechanical and process installations, including major headworks, grit system, influent, and effluent piping activities, as well as installation of the grit removal headcell and associated equipment.
- Continued electrical and instrumentation works throughout the facility, including conduit, wiring, lighting, panel installations, and Automatic Transfer System.
- Progressed interior construction activities, including steel stud framing, drywall installation, painting, inspections chambers, and coordination of site grading, pavement removals, and winter access requirements.



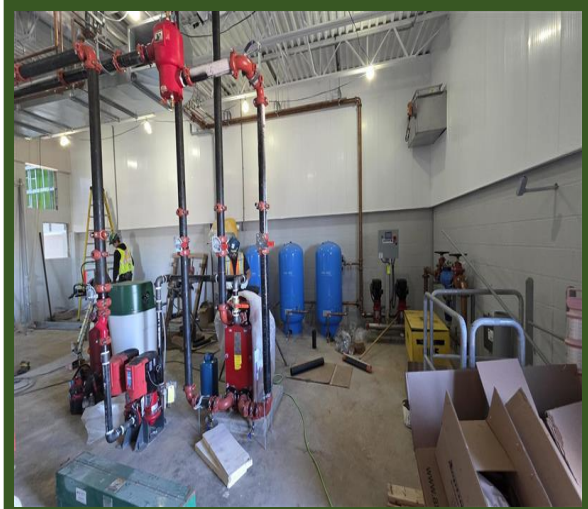



ENGLOBE
